




Hangzhou Xixi Building Company LTD.


希希建筑

Project: PTSV038 (171201)			Building Area (㎡) : 64			2017/12/1	
		Materials	Unit	Quantity		Remark	
1	A	FOB Total Price		\$23,726			
4	I	Main Frame Cost					
5		LGS frame	kg	2720		G550-AZ150	
7		Subtotal		\$4,597			
8	II	Maintance Cost					
9		Roof Panel	㎡	Color steel roof tile	183	Roof structure as Orginal(pick out)	
10			㎡	Housewrap	201		
13			㎡	100mm glass fiber insulation	201		
14		Exterior Wall	㎡	12mm Cement-fiber+paint	122		
15			㎡	Housewrap	134		
18			㎡	12mm OSB board	122		
19			㎡	100mm glass fiber insulation	122		
20			㎡	12mm gypsum board	101		
21			㎡	12mm fiber cement	21		
25			Interior wall	㎡	12mm gypsum board		
26		㎡		12mm fiber cement	41		
27		㎡		Housewrap	45		
28		㎡		100mm glass fiber insulation	93		
29		Tiles for WC wall	㎡	300*450mm	62	300*450mm ceramic	
30		Ceiling	㎡	outdoor	26	0.5mm steel sheet	
31			㎡	indoor-1	24	steel sheet for W.C. and balcony	
32			㎡	indoor-2	95	9mm gypsum board	
33		Floor	㎡	Floor-1	90	12mm laminated floor	
34			㎡	Floor-2	24	300*300mm ceramic tile for W.C and kitchen	
35			m	Skirting	110	1.2mm PVC	
36		Window	pc	Window 1	1	Aluminum alloy fixed window with single glass: 600*600mm	
37			pc	Window 2	1	Aluminum alloy fixed window with single glass: 800*600mm	
			pc	Window 3	3	Aluminum alloy sliding window with single glass :1500*1100mm	
38			pc	Window 4	1	Aluminum alloy sliding window with single glass :1800*1100mm	
39		Door	pc	Door 1	1	Steel security door:900*2080mm	
			pc	Door 2	1	Aluminum alloy tempered glasses sliding door with double glasses:2000*2150mm	
40			pc	Door 3	3	MDF panel door:800*2100mm	
41			pc	Door 4	2	MDF panel door700*2100mm	
42		For Kitchen	㎡	12mm OSB board	14	12mm OSB board for kitchen	
43		Flashing	㎡		21	self-folded steel sheet	
44		Verge board	m		52	steel sheet	
45		Alu. Profile	kg		55	for corners and door & window...	
46		Subtotal		\$12,817			
47	III	Fittings cost					
48		Hardware	Unit		1		
50		Silicon	Unit		0.5		
51		Plumbing	m	Water pipe	16	80*80mm PVC	
52			m	Gutter	36.4	PVC	
53			Unit	Inlet & outlet	1	For one kitchen, one toilet	
54		Sanitary	Unit	Washbasin	1	ceramic	
55			Unit	Shower room	1	0.9*0.9*2m	
56			Unit	Toilet	1	ceramic	
57		Kitchen	Unit		1	4.0*0.6m	
58		Conduit	m		250	PVC	
62		Subtotal		\$2,198			
63	IV	Transportation cost					
64		Packing rack	Unit	1.00		For packing	
65		40'HQ	Unit	0.67		Factory to Ningbo port,2*40'HQ can load 3 units	
66	V	Subtotal		\$1,019			

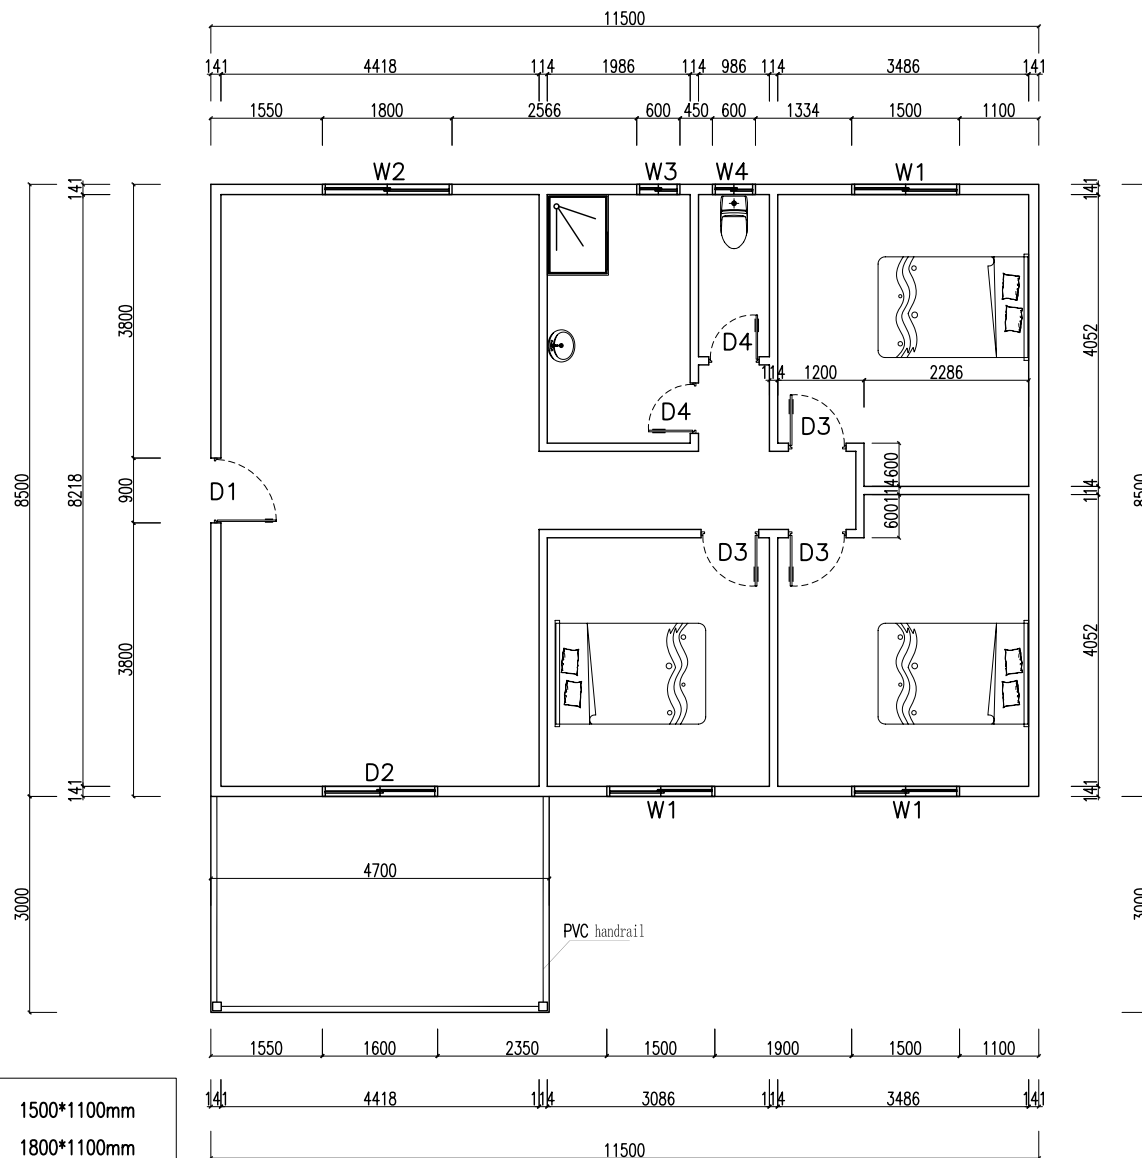


Aluminum alloy sliding window:W1	1500*1100mm
Aluminum alloy sliding window:W2	1800*1100mm
Aluminum alloy sliding window:W3(with patterned glassess)	600*800mm
Aluminum alloy sliding window:W4(with patterned glassess)	600*600mm
Steel security door:D1	900*2080mm
Aluminum alloy sliding tempered glasses door:D2	1600*2100mm
MDF panel door:D3	800*2100mm
MDF panel door:D4	700*2100mm

Project name 工程名称	Project No. 工程编号	Designer 设计人	Drawer 制图员	Assessor 审核	Page 图号
轻钢住宅	PTXV877	沈晓	沈晓	张益峰	01
		Category 设计阶段	Proofreader 校对	Date 日期	Proportion 比例
	平面布置图	PROPOSAL	王开亚	2014.11.08	1:60

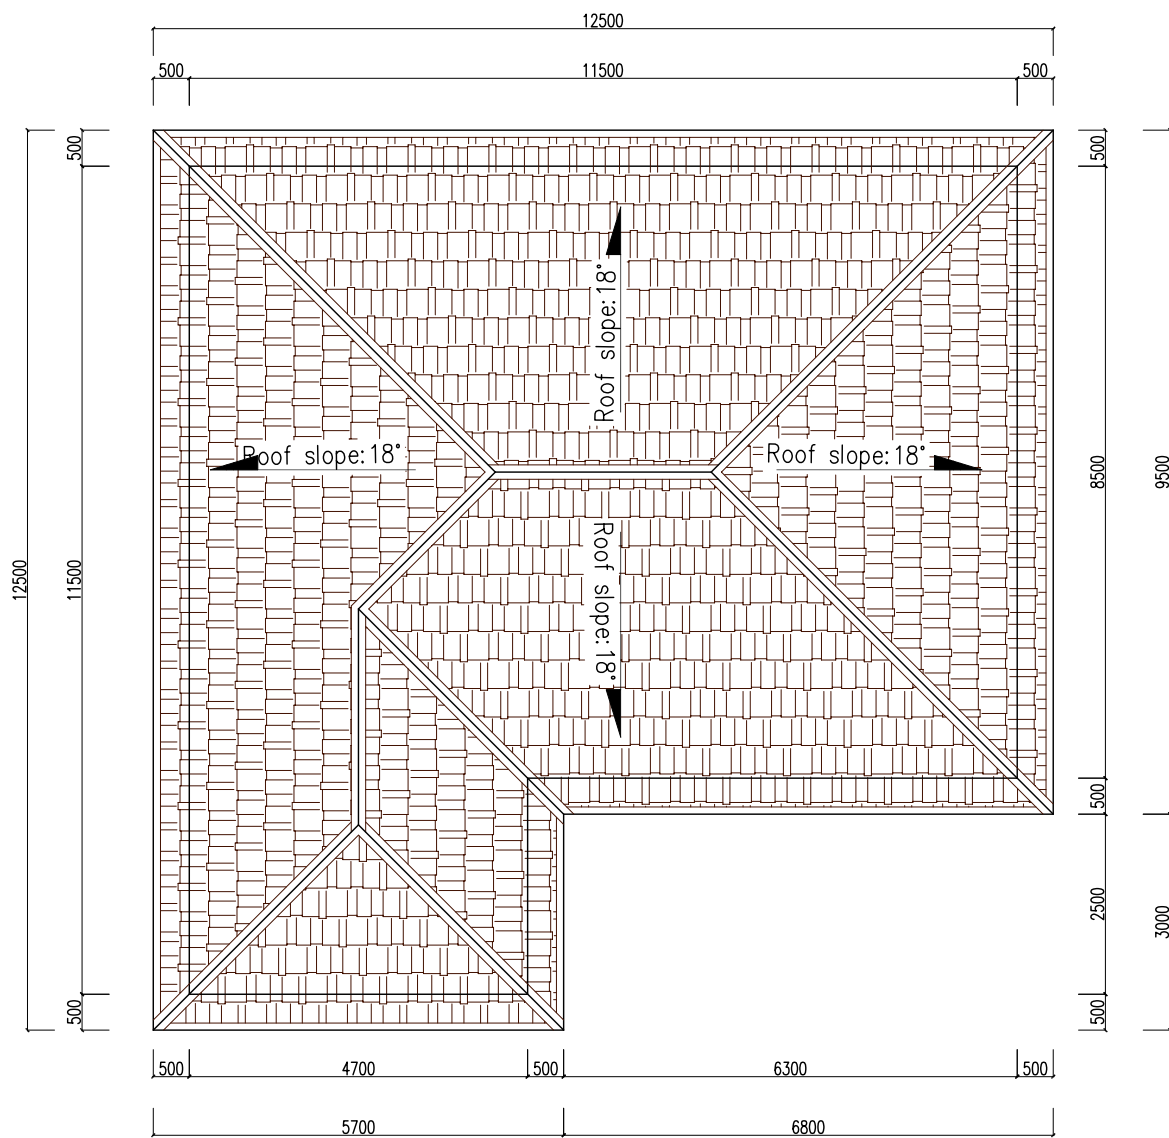


Layout for roof plan

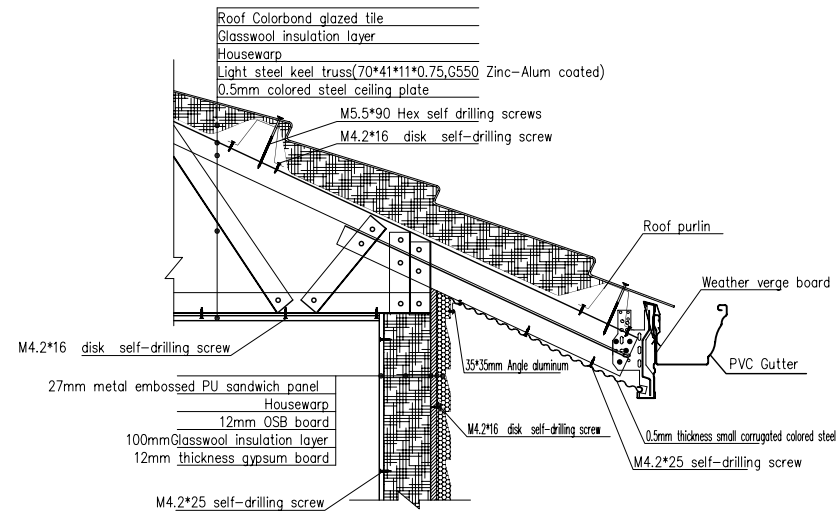


Details for roof and eave


Project name 工程名称	Project No. 工程编号	Designer 设计人	Drawer 制图人	Assessor 审核	Page 页号
轻钢住宅	PTXV877	沈耀	沈耀	张益峰	02
Item 图纸名称	Category 设计阶段	Proofreader 校对	Date 日期	Proportion 比例	
屋面布置图	PROPOSAL	王开亚	2014.11.08	1:60	

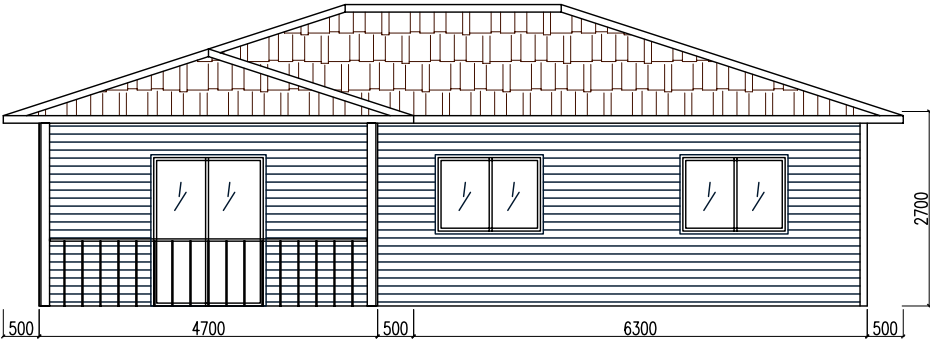


South Elevation

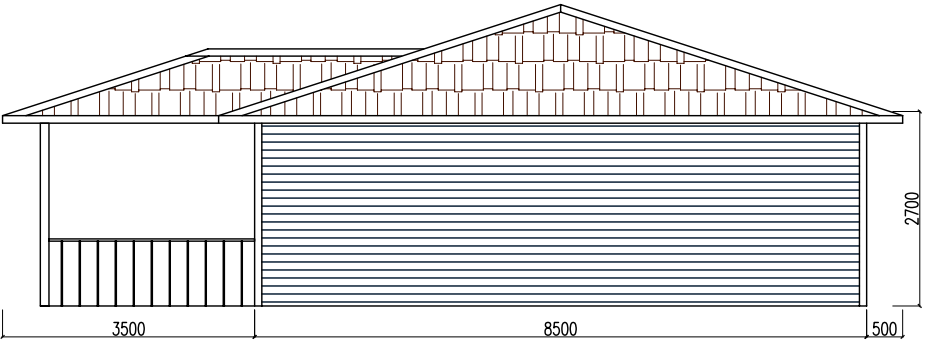

East Elevation

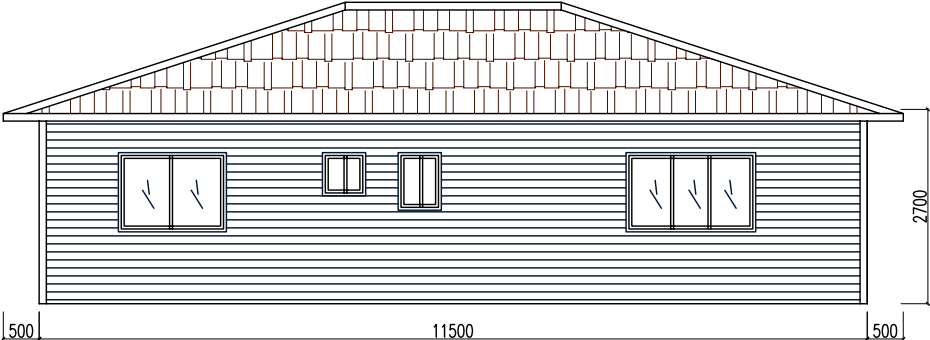


North Elevation

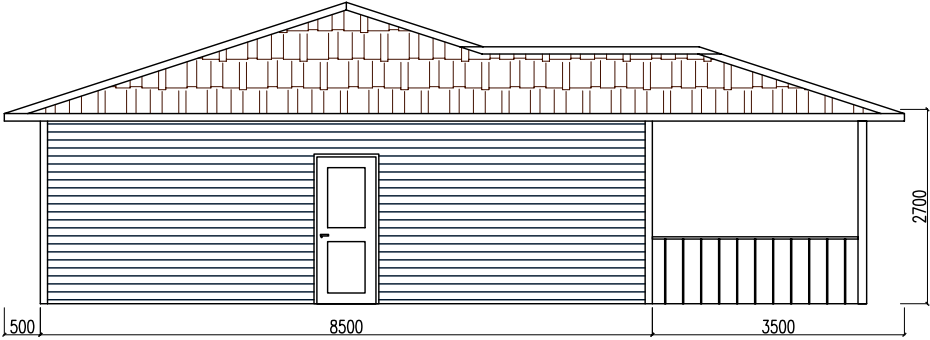


West Elevation


Project name 工程名称	Project No. 工程编号	Designer 设计师	Drawer 制图员	Assessor 审核	Page 页号
轻钢住宅	PTXV877	沈耀	沈耀	张益峰	03
Item 图纸名称	Category 设计阶段	Proofreader 校对	Date 日期	Proportion 比例	
立面布置图	PROPOSAL	王开亚	2014.11.08	1:60	

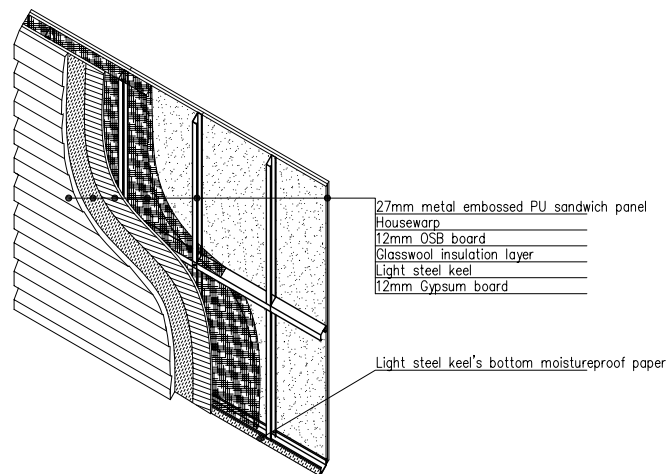

Details for outside wall

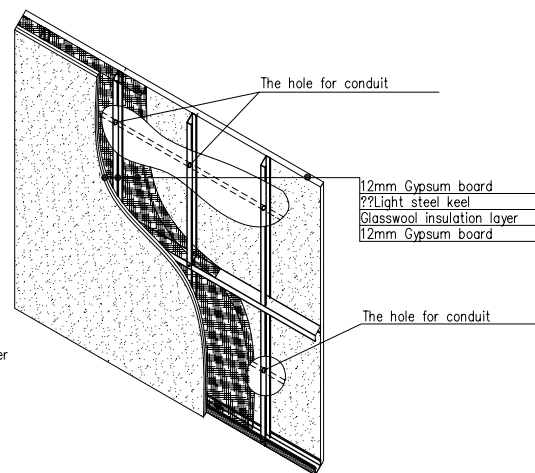

Details for inside wall

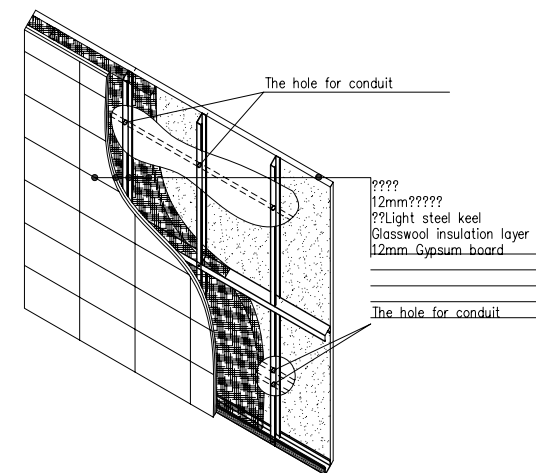

The details for toilet and kitchen wall

Project name 工程名称	Project No. 工程编号	Designer 设计人	Drawer 制图人	Assessor 审核	Page 页号
轻钢住宅	PTXV877	沈耀	沈耀	张益峰	04
图纸名称	墙面详图	设计阶段	校对	日期	比例
		PROPOSAL	王开亚	2014.11.08	1:60
